



Final Project
CCSW 313 Software Project Management
Section: SE3
Eventure Jeddah

Team Members:

Enas Alqarni 2314104

Jana Akkad 2313200

Abrar Alharbi 2317129

Table of Contents

Stage 1	3
Business Case Analysis	3
1.0 Introduction/Background	3
2.0 Business Objective	3
3.0 Current Situation and Problem/Opportunity Statement	3
4.0 Critical Assumptions and Constraints	3
5.0 Analysis of Options and Recommendation	3
6.0 Competitive Market Research	4
7.0 Preliminary Project Requirements	4
8.0 Budget Estimate and Financial Analysis	4
9.0 Schedule Estimate	5
10.0 Potential Risks	5
11.0 Exhibits	6
12.0 SWOT Analysis	7
Software Requirements Specification (SRS) for Eventure Jeddah	8
1.0 Functional Requirements	8
2.0 Non-Functional Requirements	9
Stakeholder Register Report Table	10
Stakeholder Management Strategy	11
Project Charter	12
Kick-off Meeting	14
Stage 2	15
Scope Statement	15
Work Breakdown Structure of the Project	17
Gantt Chart	19
Network Diagram	22
Cost Estimation	23
Our Logo	24
Conclusion and Lessons Learned	25

Stage 1

Business Case Analysis

1.0 Introduction/Background

Eventure Jeddah is a bilingual (Arabic/English) mobile application designed to centralize and simplify the discovery, planning, and attendance of events across Jeddah. Currently, information about local events is dispersed across WhatsApp groups, Instagram stories, and institutional email chains, which limits discoverability and engagement. Eventure Jeddah solves this problem by aggregating event data from student clubs, universities, cultural centers, and local businesses into one intuitive platform.

2.0 Business Objective

- Foster stronger community engagement
- Empower students and local organizers by enhancing their event outreach
- Support Jeddah's tourism and cultural branding
- Generate revenue through premium event listings, targeted ads, and partnerships

3.0 Current Situation and Problem/Opportunity Statement

The current method of promoting events in Jeddah is fragmented and informal. Most events are discovered through:

- Social media stories (which disappear)
- Private group messages (not publicly searchable)
- Word of mouth or email chains

There is a lack of a dedicated, bilingual platform that serves as a city-wide event discovery and planning hub. This project presents an opportunity to offer a smart, centralized solution tailored to the cultural and linguistic needs of Jeddah's population.

4.0 Critical Assumptions and Constraints

- The app must be accessible and usable in both Arabic and English
- The budget is fixed at \$130,000
- The project must launch by November 13, 2025
- Must operate smoothly on both Android and iOS (Android 10+, iOS 13+)
- Collaboration is expected with universities and cultural centers for event data

5.0 Analysis of Options and Recommendation

1. Do Nothing: Events will remain scattered, user engagement will be minimal, and Jeddah will lack a centralized event identity.
2. Partner with existing platforms like Eventbrite or Meetup: These platforms do not offer bilingual support or local event filtering.
3. Build a dedicated bilingual app in-house (Recommended): Custom-built, allows tailored features, city branding, and local partnerships.

Recommendation: Option 3 is the best strategic fit given the market gap.

6.0 Competitive Market Research

- Eventbrite: Widely used internationally but lacks Arabic support and localization for Saudi cultural needs. Lacks deep integration with local events and student clubs.
- Meetup: Popular for niche communities but less effective for large-scale public events, and again, lacks Arabic and Jeddah-specific features.
- Jeddah Today (Instagram): Good for visibility, but not structured or searchable. Relies heavily on manual story updates.

Conclusion: No existing platform combines bilingual UI, smart filtering, GPS-based event navigation, and academic/community partnerships the way Eventure Jeddah does.

7.0 Preliminary Project Requirements

- User registration and secure login
- Event browsing by category, date, and location
- RSVP, notifications, and calendar sync
- GPS event navigation
- Event submission for organizers with admin approval
- Arabic/English support
- Cloud-based backend and admin dashboard

8.0 Budget Estimate and Financial Analysis

Budget: \$130,000 total

Includes:

- Development & UI/UX: \$65,000
- Cloud infrastructure: \$20,000
- Marketing: \$20,000
- Testing and QA: \$15,000
- Miscellaneous: \$10,000

Projected Benefits:

- Ad revenue & partnerships: \$100,000/year
- Premium listings: \$50,000/year

$ROI = 130,330 / 130,000 = 1.002 = 100\%$

Payback Period: < 1 year (around 10.4 months)

NPV: Positive, assuming 10% discount rate and 3-year lifespan

9.0 Schedule Estimate

Start: May 5, 2025

End: November 13, 2025

Duration: 193 days

10.0 Potential Risks

Risk	Impact	Probability	Mitigation Strategy
Low user adoption	High	Medium	Partner with universities and cultural centers to seed content
Technical bugs or app crashes	Medium	Low	Rigorous testing and staged rollout
Inconsistent event data	Medium	Medium	Admin panel for vetting and curating content
Data privacy concerns	High	Medium	Implement secure authentication and transparent policies
Competitor market entry	Medium	High	Prioritize localized features and bilingual UI

11.0 Exhibits


Exhibit A: Financial Analysis

NPV, ROI & payback analysis


Financial Analysis for Project eventure					
Created by:		Date:			
Note: Change the inputs, shown in green below (i.e. interest rate, number of years, costs, and benefits). Be sure to double-check the formulas based on the inputs.					
Discount rate	10.00%				
Assume the project is completed in Year 0			Year		
	0	1	2	Total	
Costs	130,000	0	0	130,000	
Discount factor	1.00	0,909	0,826		
Discounted costs	130,000	0,00	0,00	130,000	
Benefits	0	150,000	150,000	130,000	
Discount factor	1.00	0,909	0,826		
Discounted benefits	0	136,350	123,900	260,250	
Discounted benefits - costs	(130,000)	136,350	123,900	130,250	← NPV
Cumulative benefits - costs	(130,000)	6350,00	130,250	6600	
ROI	100%				
			Payback in Year 1		
Assumptions					
Enter assumptions here					

Dis rate 10%

project1	Year0	Year1	Year2	Total
Ben	0.00	150.000	150.000	300,000
cost	130,000	0,00	0,00	130,000
cash flow	(130,000)	150,000	150,000	170,000
npv	130,330			

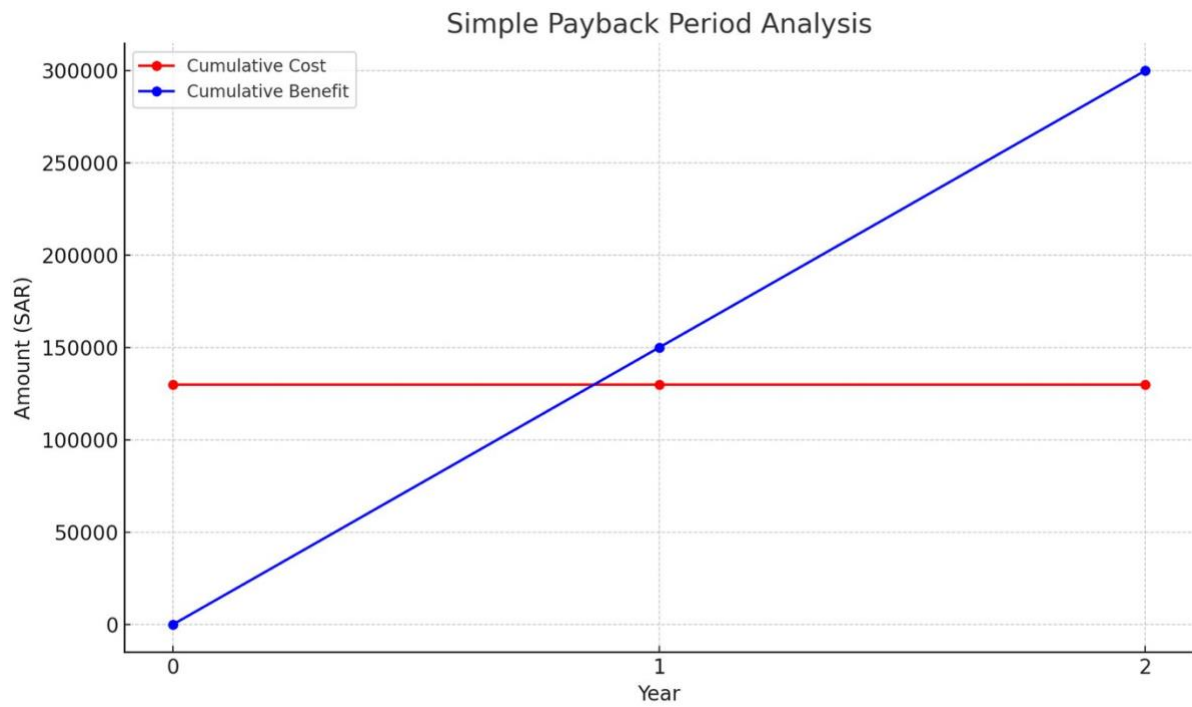

12.0 SWOT Analysis

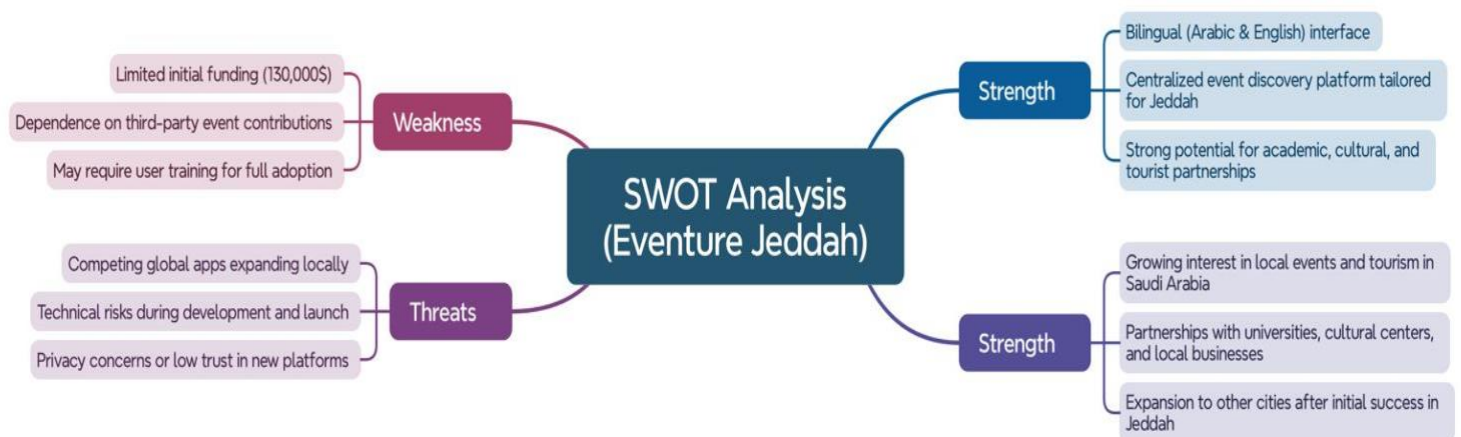

Presented with **xmind**

Software Requirements Specification (SRS) for Eventure Jeddah

1.0 Functional Requirements

ID	Functional Requirement Description
FR1	The system shall allow users to create an account and securely log in.
FR2	The system shall allow users to browse available events by category and date.
FR3	The system shall allow users to search for events by keywords or location.
FR4	The system shall allow users to RSVP to selected events.
FR5	The system shall send notifications and reminders for RSVP'd events.
FR6	The system shall provide GPS navigation to the event location.
FR7	The system shall allow users to add events directly to their device's calendar.
FR8	The system shall allow event organizers to submit events through a form for approval.
FR9	The system shall allow the admin to approve, edit, or reject submitted events.
FR10	The system shall support full Arabic and English language interfaces for all users.

2.0 Non-Functional Requirements

ID	Category	Non-Functional Requirement Description
NFR1	Usability	The system shall have a user-friendly and intuitive user interface.
NFR2	Performance	The system shall load the events listing within 2 seconds under standard network conditions.
NFR3	Availability	The system shall maintain a monthly uptime of at least 99.5%.
NFR4	Security	The system shall securely encrypt user data during transmission and storage.
NFR5	Scalability	The system shall support scalability to accommodate 10,000 concurrent users.
NFR6	Localization	The system shall provide bilingual support for Arabic and English users.
NFR7	Integration	The system shall integrate seamlessly with Google Maps and Calendar APIs.
NFR8	Compatibility	The system shall ensure compatibility with Android 10+ and iOS 13+ devices.
NFR9	Notifications	The system shall provide push notifications for reminders without delay or failure.
NFR10	Data Management	The system shall perform regular backups of event and user data to prevent data loss.

Stakeholder Register Report Table

Name	Position	Internal/External	Project Role	Contact Information
Wed Abo Zenada	Course & Lab Instructor	Internal	Main Investor	wed.zenada@uj.edu.sa
Enas Algarni	Team Leader	Internal	Project Manager	Enas.alqarniii@eventure.dev
Abrar Alharbi	Backend Developer	Internal	Team Member	abrarharbi@eventure.dev
Amina Mulla	UI/UX Designer	External	Subcontractor	amina.designs@freelance.com
Omar Al Harbi	Technical Consultant	External	Advisor	omar.consult@techpartners.com
Jana Akkad	QA Specialist	Internal	Team Member	janaakkad@eventure.dev
Mohammed Alsubhi	Business Investor	External	Financial Sponsor	Mohammed.subhi@venturegroup.com
Lmeaa Alsubhi	Marketing Consultant	External	Advisor	lmeaa.marketing@brandboost.com
Ahmed Al Zahrani	Cloud Engineer	External	Hosting & Infrastructure	ahmed.cloud@aws.sa
Event Users (Students & Tourists)	General Users	External	Target Audience	N/A

Stakeholder Management Strategy

Name	Level of Interest	Level of Influence	Information about Stakeholder	Potential Management Strategies
Wed Abo Zenada	High	High	Main investor and course/lab instructor. Very influential academically and financially for the success of the project.	Schedule regular syncs, share milestone reports, and involve in key decisions to show academic and business impact.
Mohammed Alsubhi	Low	High	External business investor, interested mainly in financial return and project profitability.	Keep updated through quarterly financial summaries and visual ROI tracking to maintain funding confidence.
Event Users (Students & Tourists)	High	Low	Primary users of the app. Care deeply about usability and content but have no direct decision-making power.	Gather feedback via surveys, prioritize usability, and engage through social media to keep satisfaction high.
Amina Mulla	Low	Low	Freelance UI/UX designer contracted for visual tasks. Has little involvement beyond design delivery.	Assign clear, limited UI tasks with due dates and ensure she's only looped in when needed. Keep communication minimal but respectful.

Project Charter

Project Title: Eventure Jeddah Mobile Application

Project Start Date: May 5, 2025.

Projected Finish Date: November 13, 2025

Budget Information: \$130,000 has been allocated for this project. The budget includes development, marketing, cloud infrastructure, and testing costs.

Project Manager: Enas Alqarni, 0555678437, Enas.alqarniii@eventure.dev

Project Objectives:

Develop a bilingual (Arabic/English) mobile application to centralize and simplify the discovery, planning, and attendance of events in Jeddah. The app will allow users to:

- View real-time event listings
- RSVP and receive notifications
- Navigate to events via GPS
- Add events to calendars
- Submit and manage events (for organizers)

Strategic goals include fostering community engagement, empowering local organizers, supporting tourism, and generating revenue through ads and partnerships.

Main Project Success Criterion:

Achieve a 30% return on investment within the first two years and build a sustainable user base of 10,000+ within 12 months of launch.

Approach:

- Conduct competitive research and user needs surveys
- Define software requirements (functional and non-functional)
- Use agile development with iterative user testing
- Implement dual-language support and localization
- Partner with local organizations to seed event content
- Plan a phased rollout with comprehensive QA testing
- Launch with a marketing and outreach campaign
- Monitor usage and revenue metrics post-launch

Roles and responsibilities

Name	Role	Position	Contact information
Wed Abo Zenada	Sponsor	Course & Lab Instructor	wed.zenada@uj.edu.sa
Enas Alqarni	Project Manager	Team Leader	Enas.alqarniii@eventure.dev
Abrar Alharbi	Team Member	Backend Developer	abrarharbi@eventure.dev
Amina Mulla	Subcontractor	UI/UX Designer	amina.designs@freelance.com
Omar Al Harbi	Advisor	Technical Consultant	omar.consult@techpartners.com
Jana Akkad	Team Member	QA Specialist	janaakkad@eventure.dev
Mohammed Alsubhi	Financial Sponsor	Business Investor	mohammed.subhi@venturegroup.com
Lmeaa Alsubhi	Advisor	Marketing Consultant	lmeaa.marketing@brandboost.com
Ahmed Al Zahrani	Infrastructure Support	Cloud Engineer	ahmed.cloud@aws.sa

Sign-Off: Signatures of all stakeholders listed above

Comments:

- “My key concern is ensuring the app maintains bilingual usability and visual clarity throughout.” — *Amina Mulla*
- “We should validate performance and cloud reliability before marketing outreach.” — *Ahmed Al Zahrani*
- “Focus on measurable ROI and financial reporting from Day 1.” — *Mohammed Alsubhi*

Kick-off Meeting

Sunday, May 4, 2025

Project Name: Eventure

Meeting Objective:

To initiate the Eventure Jeddah project by aligning all stakeholders on the app's vision, reviewing the event platform's strategic goals and key deliverables, and setting the foundation for successful collaboration and timely execution.

Agenda

- Introductions of team members and stakeholders
- Overview of Eventure Jeddah's purpose and community impact
- Review of key project documents (business case, stakeholder register, project charter)
- Walkthrough of app features and user requirements
- Presentation of development timeline and Agile milestones
- Discussion of communication channels and quality assurance process
- Assignment of responsibilities and setting short-term deliverables

Action Item	Assigned To	Due Date
Refine project objectives	Enas Alqarni	05/05/2025
Finalize kick-off materials	Jana Akkad	07/05/2025
Define stakeholder strategies	Abrar Alharbi	09/05/2025
Review budget and timeline	Mohammed Alsubhi	08/05/2025
Prepare stakeholder register	Wed Abo Zenada	06/05/2025

Date and time of next meeting:

15/05/2025 - 1:00 PM to 2:00 PM

Stage 2

Scope Statement

Project Justification:

Eventure Jeddah is a bilingual (Arabic/English) mobile application designed to centralize the discovery, planning, and attendance of events across Jeddah, Saudi Arabia. The current landscape for event promotion in the city is fragmented, relying heavily on WhatsApp groups, social media, and institutional emails, which limits reach and engagement. No platform currently offers comprehensive coverage of Jeddah's academic, cultural, civic, and business events in both Arabic and English.

The app addresses this market gap by offering real-time listings, GPS navigation, calendar integration, and a user-friendly interface. The solution supports city branding, community engagement, student empowerment, and tourism while providing monetization through advertisements, sponsorships, and premium listings.

Product Characteristics and Requirements:

The mobile app will include the following functional and non-functional features based on the Software Requirements Specification (SRS):

Functional Requirements:

- User registration, login, and secure account management.
- Browse events by category, date, and location.
- Keyword-based search functionality.
- RSVP system and push notifications for reminders.
- GPS navigation to event venues.
- Calendar synchronization for personal planning.
- Event submission form for organizers.
- Admin approval system for event moderation.
- Full Arabic and English language support.

Non-Functional Requirements:

- Intuitive and accessible user interface.
- Load event listings within 2 seconds.
- Maintain 99.5% monthly uptime.
- Secure data transmission and encrypted storage.
- Support for up to 10,000 concurrent users.
- Seamless integration with Google Maps and Calendar APIs.
- Compatibility with Android 10+ and iOS 13+ devices.
- Regular backups for user and event data.

Summary of Project Deliverables:

1. Mobile Application (Android & iOS) with bilingual interface and core event features.
2. Admin Dashboard for reviewing and managing event content.
3. Secure Backend Infrastructure with encryption, scalability, and API integrations.
4. Wireframes and Final UI/UX Designs produced by the subcontracted designer.
5. Testing Reports covering functionality, usability, and performance.
6. Cloud Deployment on AWS (by cloud engineer).
7. Marketing Campaign Materials for app launch (via marketing advisor).
8. Training Documentation and User Manuals for admin and end-users.
9. Stakeholder Sign-Off Documents, meeting summaries, and risk mitigation plans.

Project Success Criteria:

- On-Time Delivery: Project completed and launched by November 13, 2025.
- Financial ROI: Achieve 30% return on investment within the first two years.
- User Adoption: Reach 10,000+ active users within 12 months of launch.
- App Performance:
 1. 99.5% system uptime.
 2. Event listings load in under 2 seconds.
 3. Push notifications delivered without delay.
- Stakeholder Satisfaction:
 1. Positive feedback from sponsors and course instructors.
 2. Visual and linguistic clarity maintained in both languages (as emphasized by UI/UX designer).
- Quality Assurance:
 1. Successful rollout following QA and performance validation (as advised by cloud engineer).
 2. Ongoing updates and feature improvements based on user feedback.

Work Breakdown Structure of the Project

1.0 Initiating

- 1.1 Conduct market research and identify platform gaps
- 1.2 Define strategic objectives (community, tourism, monetization)
- 1.3 Identify and document stakeholders
- 1.4 Develop and approve the project charter
- 1.5 Hold kick-off meeting and assign responsibilities

2.0 Planning

- 2.1 Finalize project scope and success criteria
- 2.2 Develop WBS and Agile timeline
- 2.3 Estimate cost and allocate SAR 130,000 budget
- 2.4 Create risk management and stakeholder strategies
- 2.5 Plan for quality assurance, testing, and communication

3.0 Executing

- 3.1 Design bilingual UI/UX
- 3.2 Develop core app features (RSVP, GPS, calendar sync)
- 3.3 Implement organizer submission and admin panel
- 3.4 Ensure full Arabic/English support and app security
- 3.5 Set up cloud infrastructure and integrations



4.0 Monitoring & Controlling



- 4.1 Conduct testing (unit, usability, performance)
- 4.2 Track budget, timeline, and risks
- 4.3 Monitor system uptime and load times
- 4.4 Collect feedback and fix bugs
- 4.5 Provide stakeholder updates



5.0 Closing

- 5.1 Perform final testing and gain approval
- 5.2 Launch app on iOS and Android stores
- 5.3 Execute marketing campaign
- 5.4 Conduct lessons learned review
- 5.5 Submit final report and close project

Gantt Chart

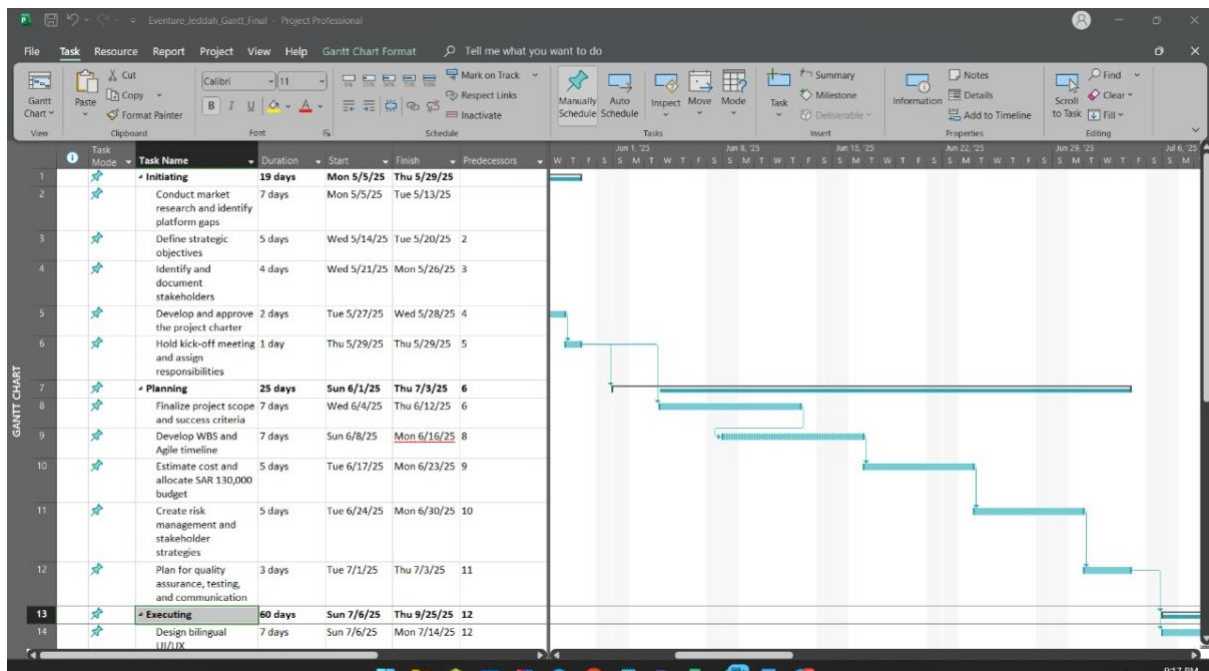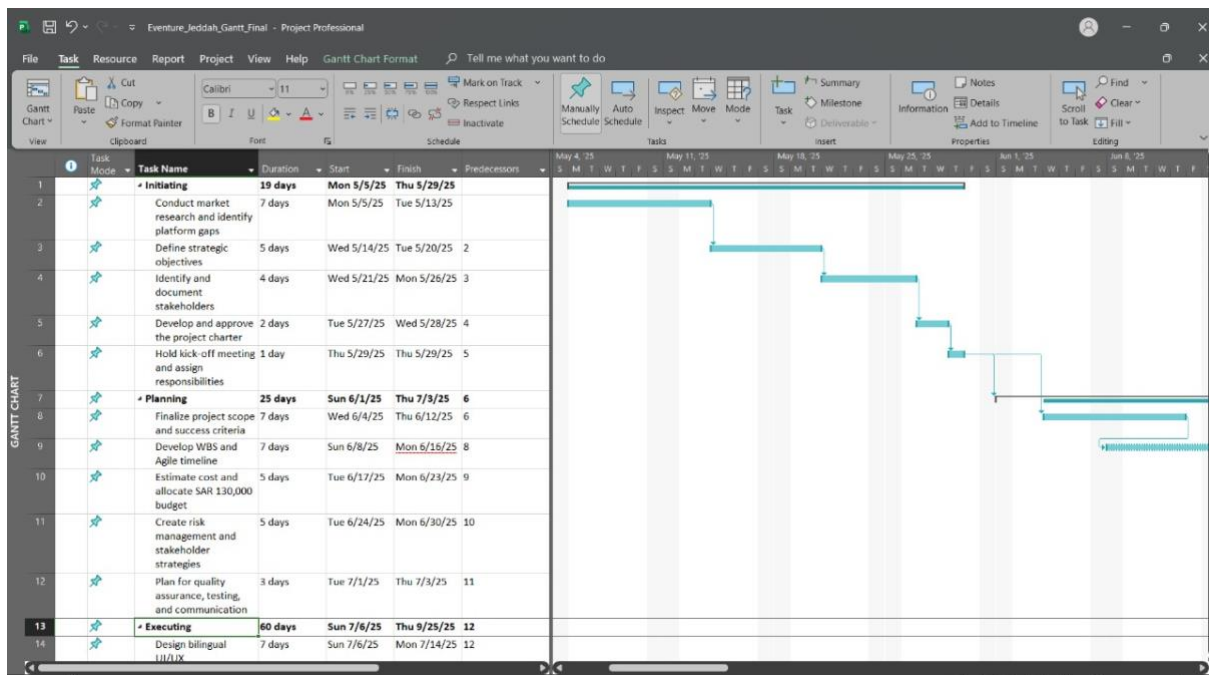

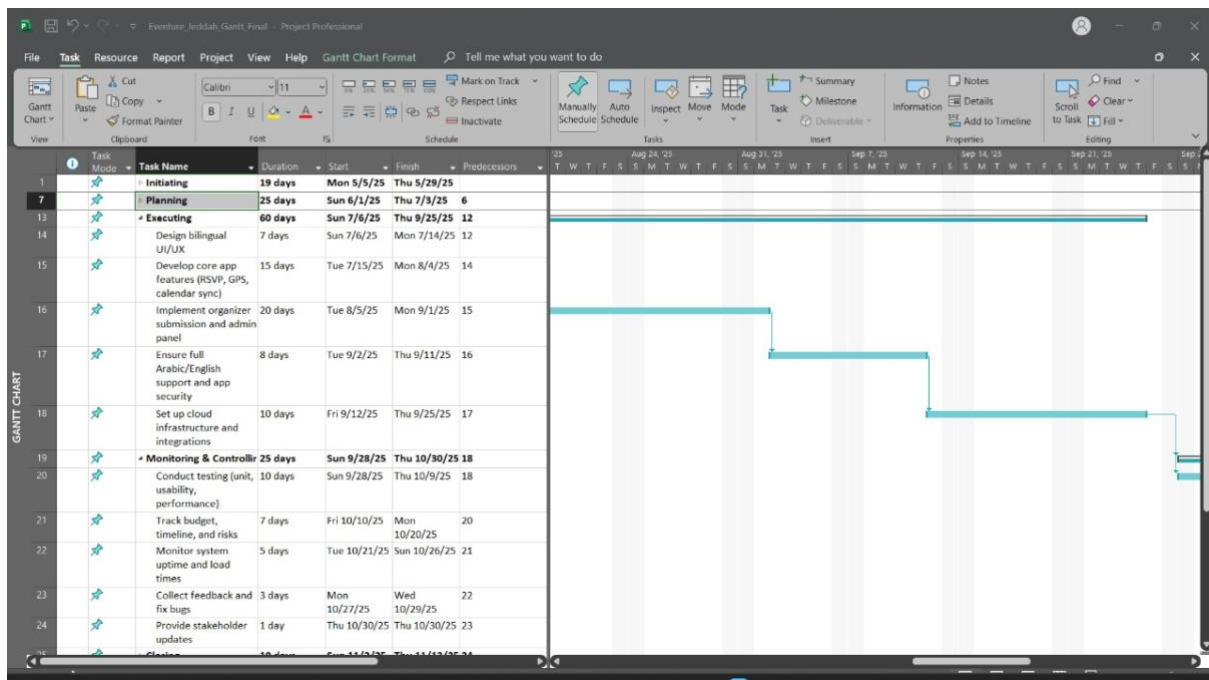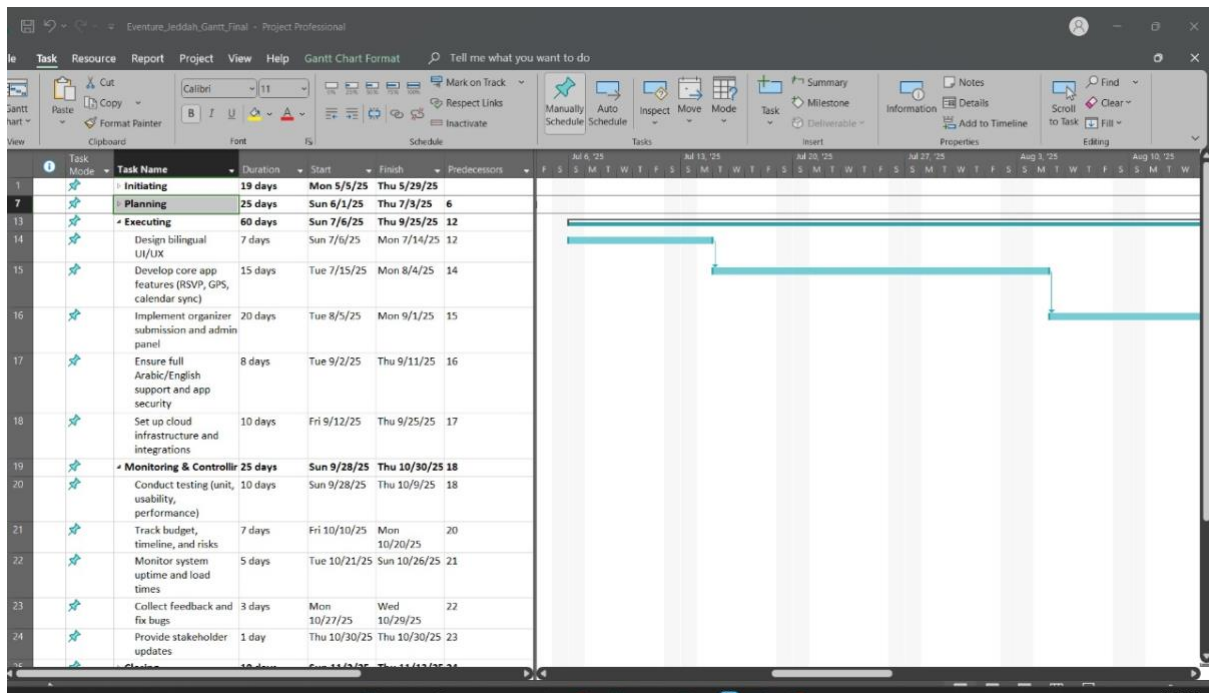

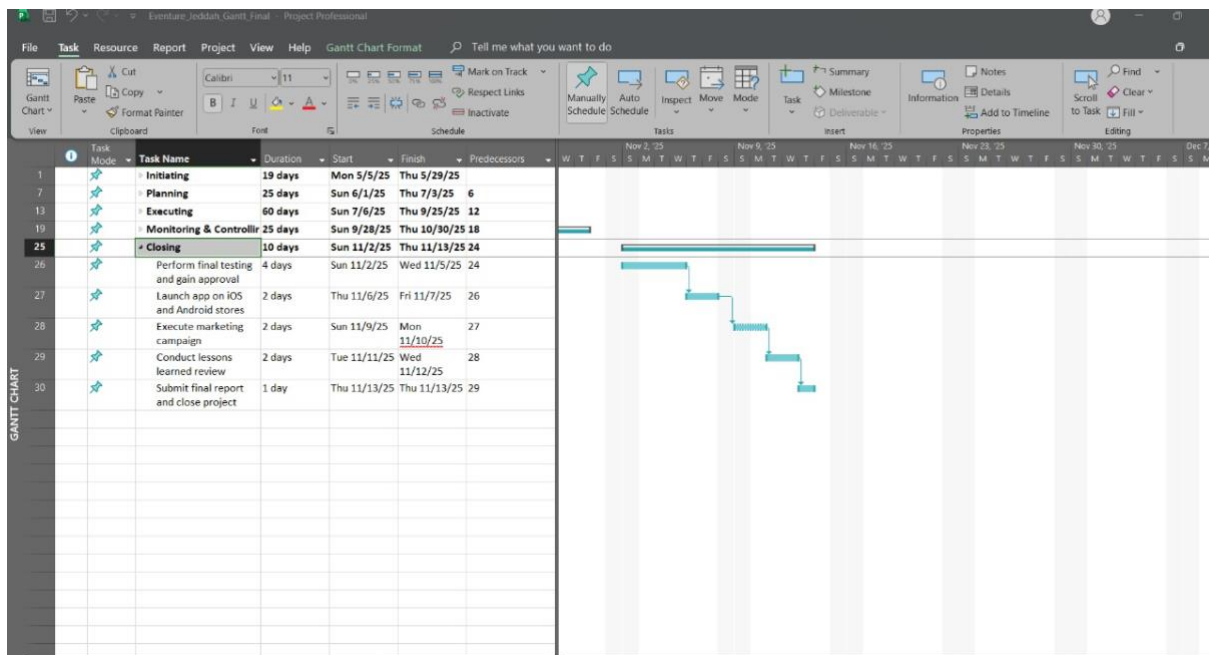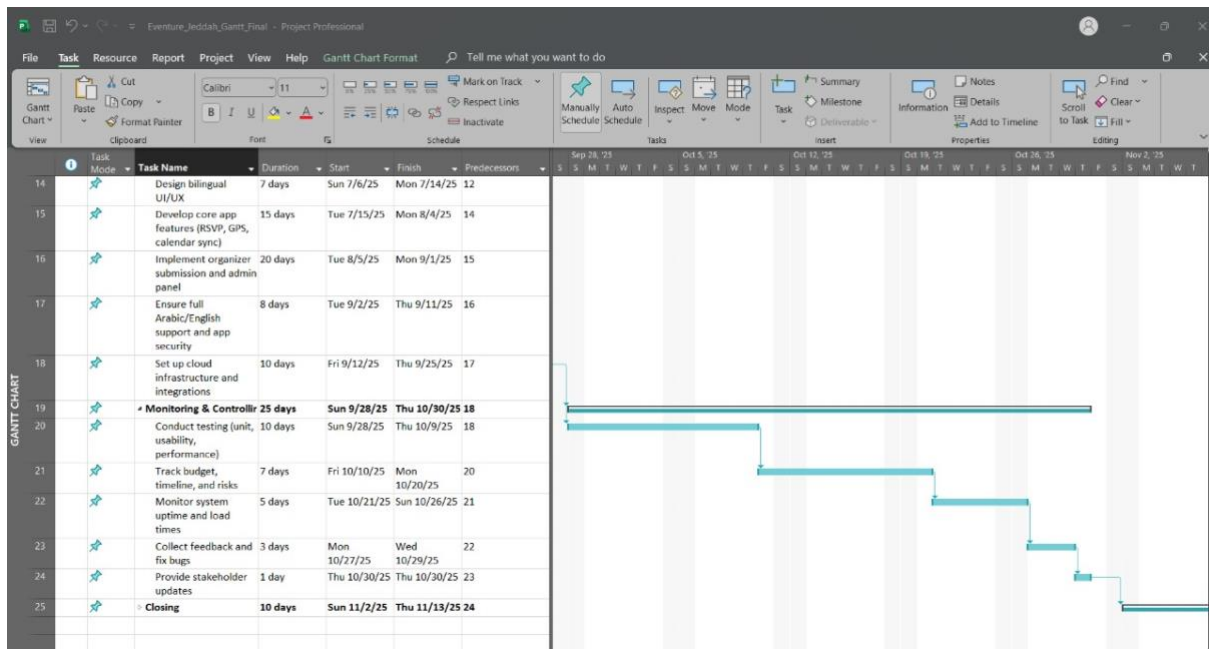

Network Diagram

The full Network diagram is uploaded with the Gantt Chart File on MS Project

Cost Estimation

	A	B	C	D	E	F
1	Eventure Jeddah Project Estimate					
2	WBS Items	# Units/Hrs.	Cost/Unit/Hr. (USD)	Subtotals (USD)	WBS Level 1 Totals (USD)	% of Total
3	1. Project Management				18600	14%
4	1.1 Project Manager	240	70	16800		
5	1.2 Planning & Coordination Tools (Jira/MS Project)	3	200	600		
6	2. UI/UX Design				9300	7%
7	2.1 Bilingual UI Designer	180	50	9000		
8	2.2 Design Software Licenses (Figma Pro)	1	300	300		
9	3. Development				62700	48%
10	3.1 Frontend Developer (iOS/Android Hybrid)	400	60	24000		
11	3.2 Backend Developer (APIs + Admin Panel)	400	75	30000		
12	3.3 Third-Party Services (e.g., Maps API, Calendar API)	1	600	600		
13	4. Infrastructure				1350	1%
14	4.1 AWS Cloud Hosting + Storage	6	200	1200		
15	4.2 Domain & SSL	1	150	150		
16	5. Testing & QA				10175	8%
17	5.1 QA Engineer (manual testing)	150	45	6750		
18	5.2 Device Testing Access	1	800	800		
19	6. Marketing & Support				3500	3%
20	6.1 Launch Campaign	1	2500	2500		
21	6.2 User Support/Helpdesk Setup	1	1000	1000		
22	7. Contingency (14.96%)				37300	15%
23	Total Estimated Cost			37300	130000	100%
24						

The cost estimate for the Eventure app was created with a clear focus on realistic and essential resources that directly match the project's scope. The total estimated cost is \$130,000, covering all major areas such as development, design, infrastructure, testing, and launch support. The highest portion of the budget (48%) was allocated to development—frontend, backend, and third-party APIs—since this is the heart of the app. Project management and UI/UX design followed with 14% and 7% respectively. We also set aside a 15% contingency to handle unexpected costs. Every amount shown is tied directly to the number of hours or units and calculated based on actual project needs, ensuring the budget is both accurate and practical.

Our Logo



The logo for Eventure creatively blends modern simplicity with event-centric symbolism. The central icon—a calendar marked with a star and surrounded by a digital network and location pin—represents event planning, discovery, and smart navigation, all of which are core features of the Eventure app. The purple and blue gradient reflects energy, innovation, and trust, aligning with the app’s mission to foster community engagement and streamline event access across Jeddah. The use of bold, rounded text keeps it youthful and accessible, mirroring the bilingual and student-friendly nature of the platform.

Conclusion and Lessons Learned

Working on the Eventure project gave us hands-on experience in planning a real mobile application from scratch. One of the most important lessons was understanding how every decision, from feature design to cost allocation, affects the overall success of the project. Building a bilingual app with local relevance meant we had to think carefully about user experience and the technologies we chose. By staying organized, communicating well, and using tools like the WBS and cost estimation sheet, we were able to stay on track. This project taught us the value of planning ahead while staying flexible to solve problems along the way.
